

PropFlo Marketing Launch Programme

Project Management Pack — CPM/PERT Schedule, Gantt, Milestones, Budget, RACI, Risk

Prepared by Interon · Commercial in confidence · Working draft (not yet approved)

All schedule figures are calculated by Critical Path Method from the project activity network. All costs ex VAT.

1. Project Summary

Structure: Two stages. Stage A (preparation) then Stage B (true 90-day live campaign). The 90-day clock starts at launch, not kick-off.
Calculated Stage A: 49 working days (~10 weeks; ~15 weeks pessimistic). Overall programme: ~159 calendar days (~5.2 months) to the Day-90 scale decision.
Critical path: compliance → landing-page copy & build → pages approval → tracking test → campaign build → pre-launch testing → launch.
Budget (ex VAT): R233,500–R283,500 across the overlap scenarios; R32,000/month management continuing after Day 90. Platform build separate.

Source of truth: CPM-PERT-MASTER-SCHEDULE.md, PROJECT-ACTIVITY-DATA.csv, PROJECT-GANTT-DATA.csv, PROJECT-COST-BASELINE.md.

2. Stage A — Preparation Overview

Milestone	Working day	~ Week	Gate
Strategy approved (M2)	18	~4	—
Compliance & claims approved (M1)	21	~5	Hard gate
Lead handling ready (M5)	26	~6	Hard gate
Landing pages approved (M3)	40	~8	Hard gate
Tracking approved (M4)	42	~9	Hard gate
Campaigns approved (M6)	45	~9	Gate
Controlled launch (M7 = Stage B Day 0)	49	~10	Launch

Calculated milestone timings (working day from authorisation). Hard gates must be true before launch.

3. Stage B — 90-Day Live Campaign Overview

Checkpoint	Live day	~ Calendar day
Launch	0	69
Day 7 technical & search-term review	7	76
Day 14 lead-quality review	14	83
Day 30 performance review	30	99
Day 45 optimisation checkpoint	45	114
Day 60 performance & channel review	60	129
Day 75 scale-readiness checkpoint	75	144
Day 90 scale decision	90	159

Live days from launch; calendar day = 69 + live day. Reviews occur after true elapsed live days.

4. PERT Network — Overview

PERT Network — Programme Overview (milestone level)

Milestone-level critical spine. Full detail in PERT-STAGE-A.svg and PERT-STAGE-B.svg.




Milestone-level critical spine. Full detail in Stage A and Stage B PERT diagrams (SVG folder).

5. Critical Path

Critical Path (Stage A)

Only zero-float activities. Any slip here moves the launch date. Durations in working days.

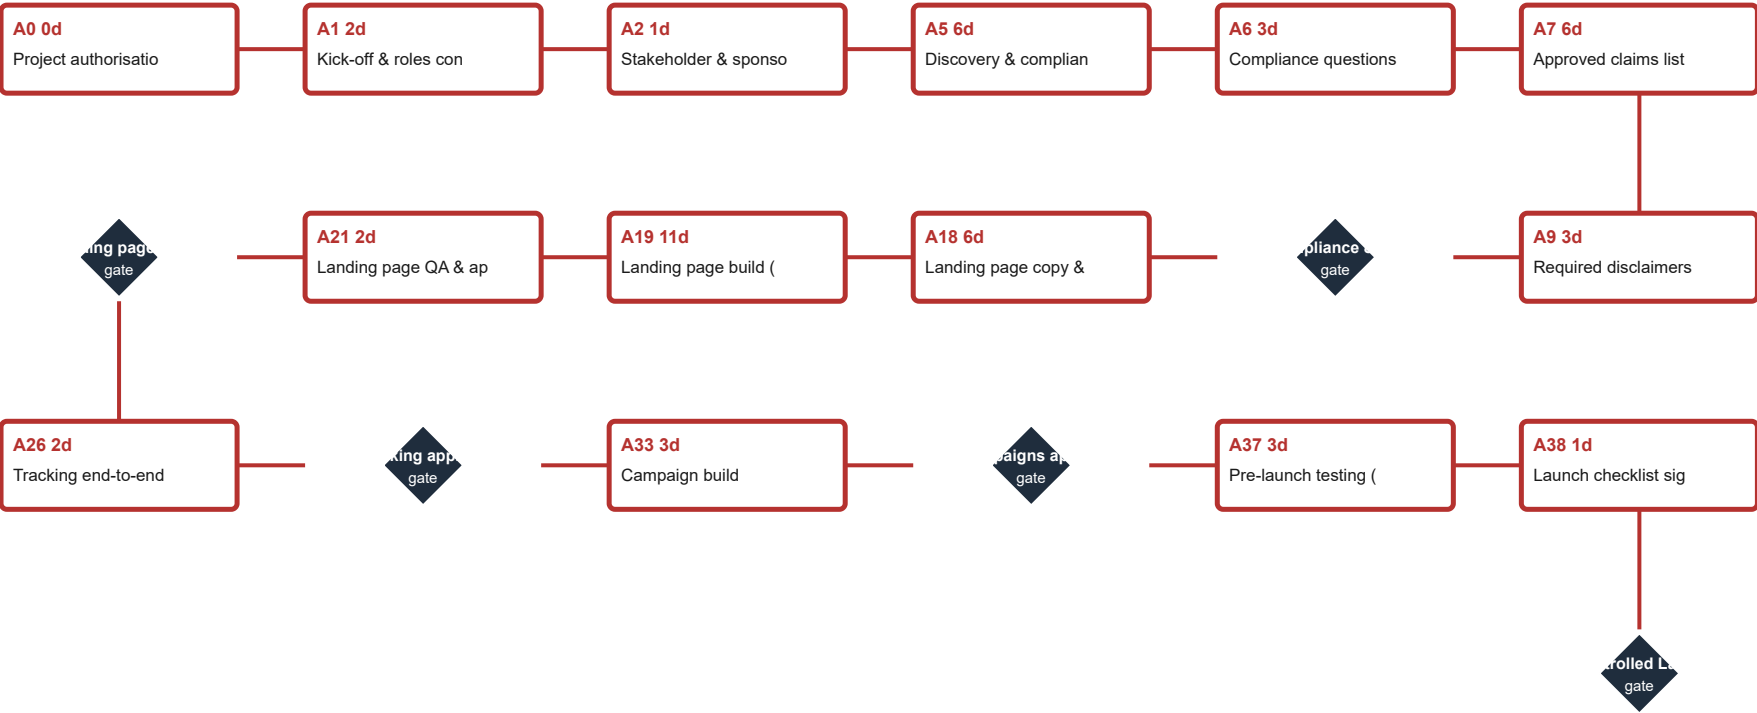


→ then STAGE B (from launch): Day 0 → Day 7 → Day 14 → Day 30 → Day 45 → Day 60 → Day 75 → Day 90 scale decision (true 90 live days).

6. Gantt — Overview

Programme Gantt — Overview

Two-stage model. Stage A preparation (Day 0–69) then true 90-day live campaign (Day 69–159). Calculated by CPM.

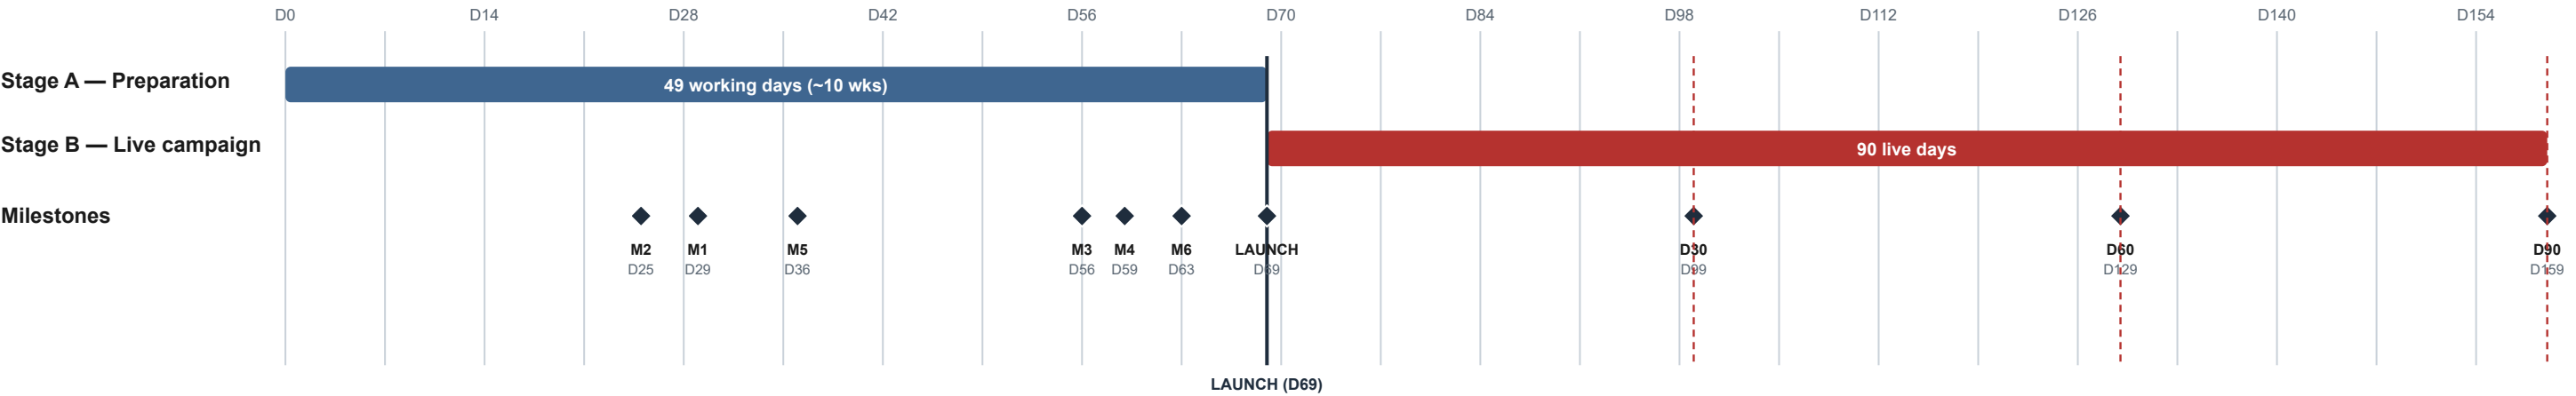

Gantt — Stage A (Preparation)


Calendar days from authorisation (Day 0). CPM early-start schedule. Launch at Day 69.




9. Milestone Timeline

Milestone Timeline

Chronological, positioned by calendar day from authorisation (Day 0). Stage B milestones are live days after launch.

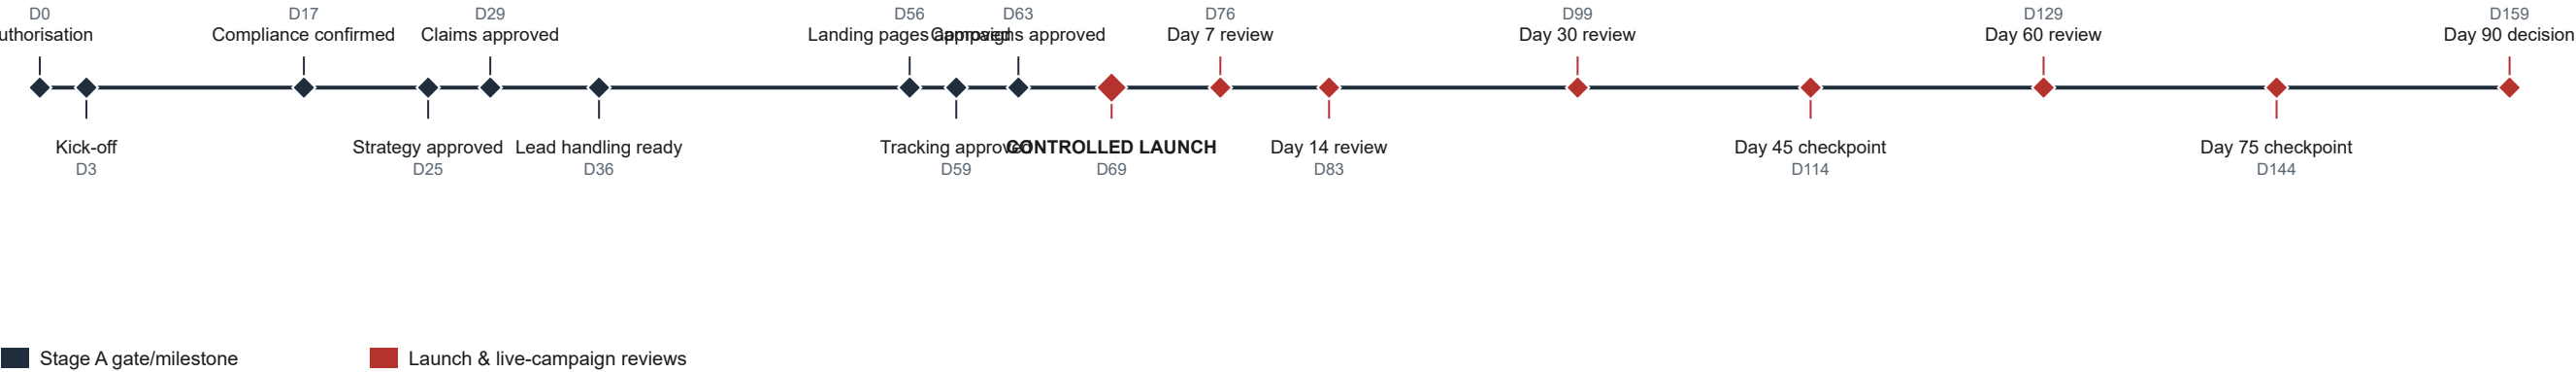

10. Budget Timeline

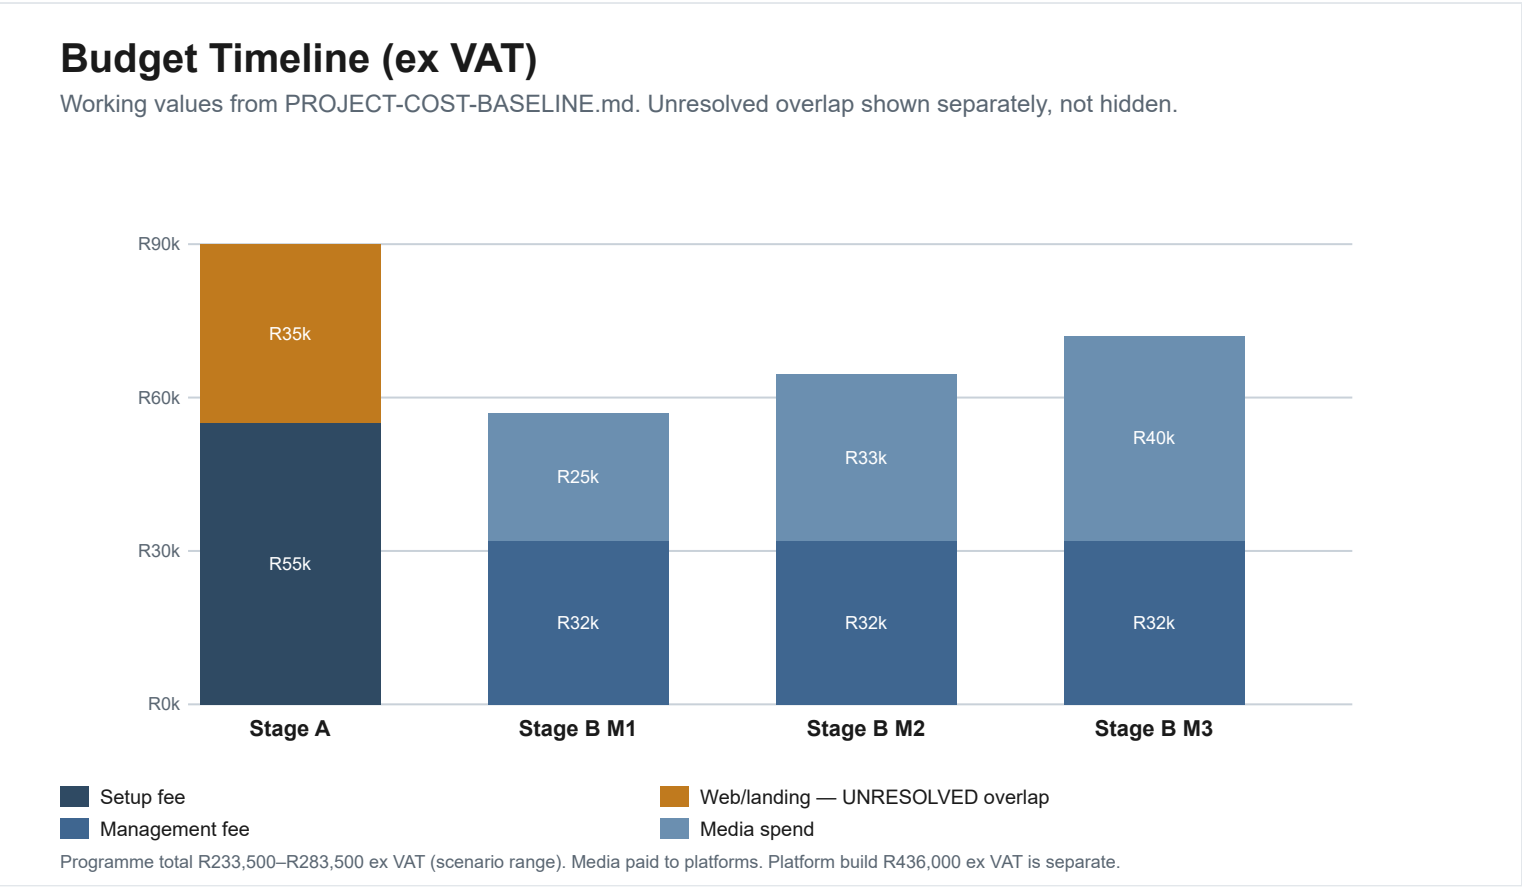

Period	Setup	Landing pages	Management	Media	Total (ex VAT)
Stage A (prep)	R40,000–R55,000	R0–R35,000 (unresolved)	R0	R0	R40,000–R90,000
Stage B Month 1	—	—	R32,000	R25,000	R57,000
Stage B Month 2	—	—	R32,000	R32,500	R64,500
Stage B Month 3	—	—	R32,000	R40,000	R72,000
Programme total					R233,500–R283,500


All ex VAT. Media paid by PropFlo to platforms. Platform build (R436,000 ex VAT) and subscriptions are separate. Landing-page/overlap ~R35,000–R50,000 is an unresolved commercial item.

11. RACI Matrix

■ R = Responsible ■ A = Accountable ■ C = Consulted ■ I = Informed

Activity	PropFlo Sponsor	PropFlo Compliance/Legal	PropFlo Sales	Interon Project Lead	Interon Strategy	Interon Paid Media	Interon Content/SEO	Interon Design	Interon Dev/Tech
Proposal and budget approval	A	C	I	R	C	I	I	I	I
Compliance and claims	A	R	C	C	C	I	C	I	I
Strategy and research	C	C	C	A	R	C	C	I	I
Website and landing pages	A	C	C	R	C	C	C	R	R
Tracking and measurement	I	I	C	A	C	R	I	I	R
Paid search	I	C	I	A	C	R	I	I	I
Meta retargeting	I	C	I	A	C	R	C	C	I
SEO and content	I	C	I	A	C	I	R	I	I
Partner and LinkedIn	C	C	C	A	R	I	C	C	I
Email and WhatsApp follow-up	I	C	R	A	C	I	C	I	I
CRM and lead management	C	I	R	A	C	I	I	I	C
Reporting and optimisation	C	I	C	A	C	R	C	I	I
Project management	A	I	I	R	C	C	C	I	I

12. Risk Matrix

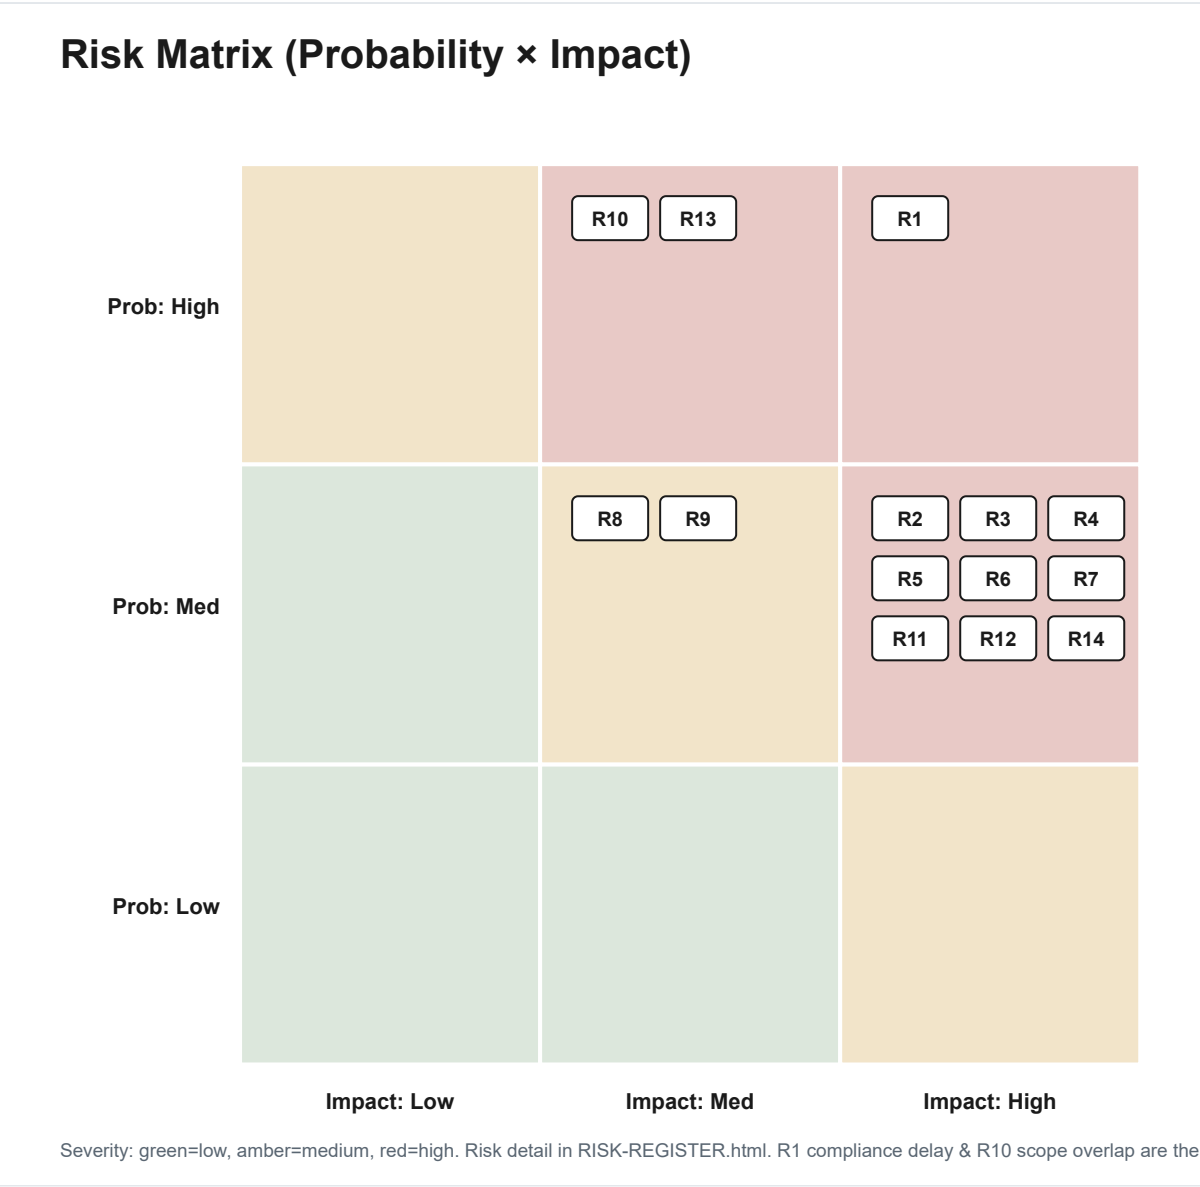

13. Risk Register

ID	Risk	Prob	Impact	Severity	Mitigation	Owner	Trigger / warning sign
R1	Compliance approval delay	High	High	High	Front-load discovery; treat as gating milestone	PropFlo Compliance	Claims not returned by ~Day 21
R2	Claims/ads rejected by platform	Med	High	High	Conservative wording; platform verification early	Interon Paid Media	Ad disapprovals; verification requests
R3	Poor landing page conversion	Med	High	High	Clear offer, trust signals, weekly form review	Interon Strategy	High traffic, low form completion
R4	Slow lead response	Med	High	High	Confirm owner and 15-min/1-hr targets before launch	PropFlo Sales	Leads uncontacted same day
R5	Poor lead quality	Med	High	High	Tight keywords, negatives, qualification form	Interon Paid Media	Many personal-loan/non-seller enquiries
R6	Insufficient sales feedback	Med	High	High	Weekly feedback loop; status discipline	PropFlo Sales	Missing outcome updates
R7	Tracking gaps	Med	High	High	Pre-launch end-to-end test; no launch until passed	Interon Dev/Tech	Events not firing in test
R8	Budget pressure	Med	Med	Medium	Controlled daily budgets; monthly review	Interon Project Lead	Spend up, qualified leads flat
R9	Advertising platform restrictions	Med	Med	Medium	Prepare documentation; expect verification	Interon Paid Media	Account/category checks
R10	Scope overlap / double charge	High	Med	High	Resolve build-vs-marketing scope before sign-off	PropFlo Sponsor	Two quotes for the same site work
R11	Delayed client approvals	Med	High	High	Approvals log; clear owners and dates	Interon Project Lead	Approvals overdue
R12	CRM / lead process failure	Med	High	High	Confirm lead stages and owner before launch	PropFlo Sales	Leads lost or unstaged
R13	Build/marketing timeline mismatch	High	Med	High	Synchronise build Phase 2 with launch, or interim pages	PropFlo Sponsor	Build not live when launch due
R14	Weak or unclear offer	Med	High	High	Confirm offer structure before spend	PropFlo Sponsor	Low conversion despite good traffic

14. Key Assumptions

- Stage A is scheduled in working days from authorisation; Stage B in live days from launch. Calendar view uses 5 working days = 7 calendar days.
- Durations use planning/PERT most-likely values and require PropFlo review; they are not confirmed facts.
- No calendar dates are set; Day 0 = authorisation.
- One Interon delivery team; no resource-levelling constraint applied.
- Compliance answers, access, and approvals are provided promptly; delays move the launch date.
- Marketing figures are ex VAT; platform-build figures are indicative and separate.
- Brand name confirmed as PropFlo. Numeric lead/application/funded-deal targets to be agreed.

15. Management Decisions Required

Unresolved commercial items — not silently resolved. See BUDGET-VALIDATION.md and PROJECT-SCHEDULE-VALIDATION.md.

- S1 / B1 — Website ownership.** Assign site, landing pages, tracking, CRM to the platform build or to marketing (recommended: hybrid interim page to protect launch). ~R35,000–R50,000 double-charge at stake.
- B2 — Management start date.** Kick-off / preparation / launch. Recommended: at launch (Stage B Day 0).
- B4 — Setup re-scope.** Trim ~R12,000–R15,000 overlapping setup lines to ~R40,000, or keep R55,000.
- B3 — Prep vs live management pricing.** Setup covers prep, or a separate prep-coordination fee.
- B5 — Ad-spend phasing.** Confirm R25k → R32.5k → R40k ramp and monthly ceiling.
- B6 — VAT basis.** Present the combined client number ex VAT (recommended), VAT as a separate line.
- B7 / S2 — Platform build.** Whether it proceeds, how it is presented with marketing, and Google financial-services verification timing.
